

Completed Renovation



Overhead View

Conceptual



Resilient Athletic Flooring

Will contain **R**idge logo




Bottle Filling Station Sustainable & Green



Folding Glass Wall


Infilled into existing overhead door opening

(View and palm trees not included)

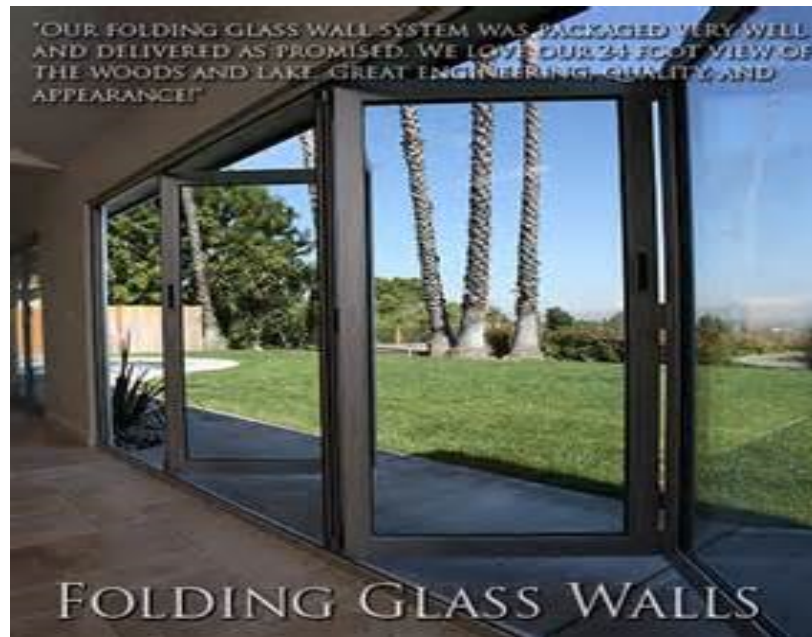

ADA lift Access

1st floor to lower level

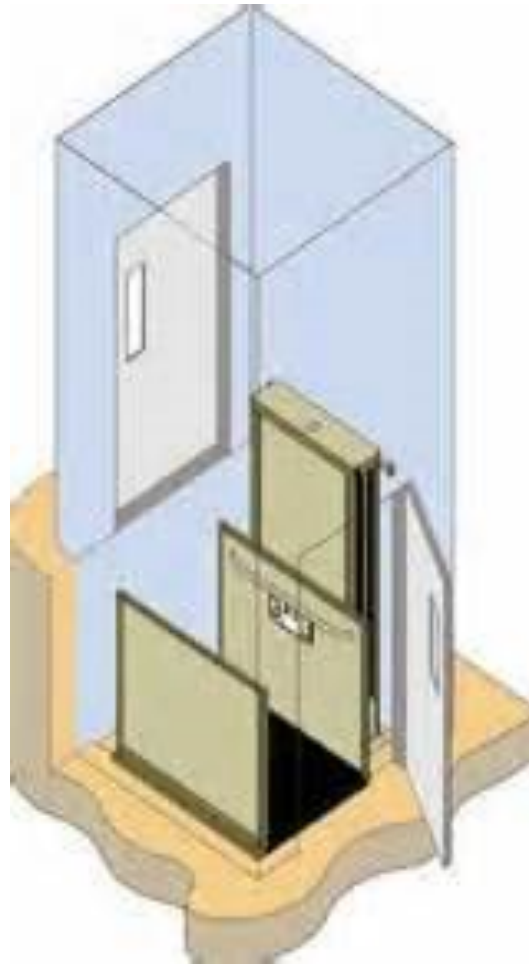

High efficiency
30% outside air rooftop A/C unit



Wellness Center

Construction Schedule

Proposed

Demolition / Preparation:

3/30/15 – Contract

4/20/15 – Order Roof top unit & ADA lift

5/01/15 – Complete All shop drawings.

Glass Door/Ductwork/Lift

6/18/15 - Ridge High School Commencement.

6/19/15 - Site Mobilization.

6/22/15 - 1 wk Demolition.

6/22/15 - Steel Fabrication

6/29/15 - 1 wk Shaft Openings

Construction:

7/1/15 - Steel Delivery

7/06/15 – Ductwork/ Electrical

7/20/15 – Installation of lift

7/27/15 – Rig Rooftop

8/03/15 – Lighting and fixtures/ Window install

8/17/15 - Flooring

8/31/15 - Finishes / RTU start up

Clean Up Demobilize

9/08/15 – Completion

Design Plan

